

NEWSLETTER 6. MAY 2016


Mc Aleen & Rushe Contracts UK have been appointed by UNITE Group plc to undertake the demolition of the existing Homebase and construction of the new mixed use development comprising of 579 bedroom Student Accommodation, Class 1 (Retail) / Class 2 (Financial, Professional & other Services) and associated facilities at 102 St Leonards Street Edinburgh.

Good progress has continued to be achieved onsite since our last Newsletter update;

- Piling works now complete
- Exposing & cropping down of the piles to enable foundations to be formed continues to progress.
- Formation of the building foundations is ongoing
- Formation of the ground floor slab now advancing
- The columns & walls from ground floor advancing
- Installation of the under slab drainage continues to advance



Completion of the overall scheme will be early August 2017 and we shall continuously strive to ensure that our works cause minimum disruption and inconvenience as possible throughout the demolition & construction phases of our project.

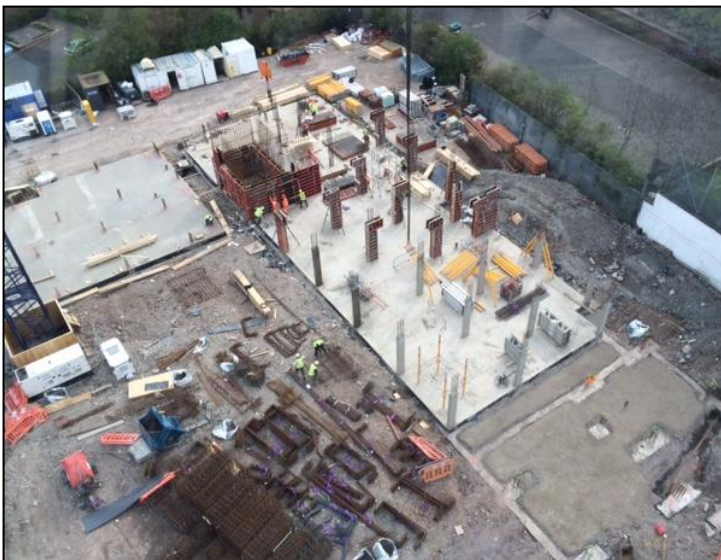

Planned Activities onsite in the coming 4 weeks include;

- Complete foundation pile caps & ground beams
- Install remaining under slab drainage across full footprint of the building
- Progress concrete pours for formation of ground floor slab
- Advance columns & walls following formation of the ground floor concrete slab

We will continue to update you every month as works progress throughout the programme. If you have any queries please do not hesitate to contact our Site Manager, Mr Stephen King at;

Email; stephen.king@mcaleen-rushe.co.uk

Tel; [07570670800](tel:07570670800)
